

Weekly Notice of Operations (WNoO)

Dogger Bank C Offshore Windfarm

Construction Operations

DOGGER BANK
WIND FARM

Issue Date: 20th June 2026

LF700013-CST-DOG-NOT-0099 Weekly Notice of Operations – Rev 095

Work Planned for the Period 20.07.2026 to 26.07.2026

Offshore Construction of the Dogger Bank C Offshore Wind Farm commenced on the 07th of October 2024.

This notice will be updated weekly, giving information on the progress and resources involved in the offshore project. The intention is to give an overview of activities and vessels involved. Should anyone have questions regarding the operations, we kindly ask you to put them forward well in advance.

Dogger Bank Offshore Wind Project is a development project within the Renewables offshore wind sector for the three owners; SSE, Equinor and Vårgrønn. Dogger Bank C is the third stage of development in the Dogger Bank Zone in the United Kingdom. It will have a consented capacity of up to 1.2 GW.

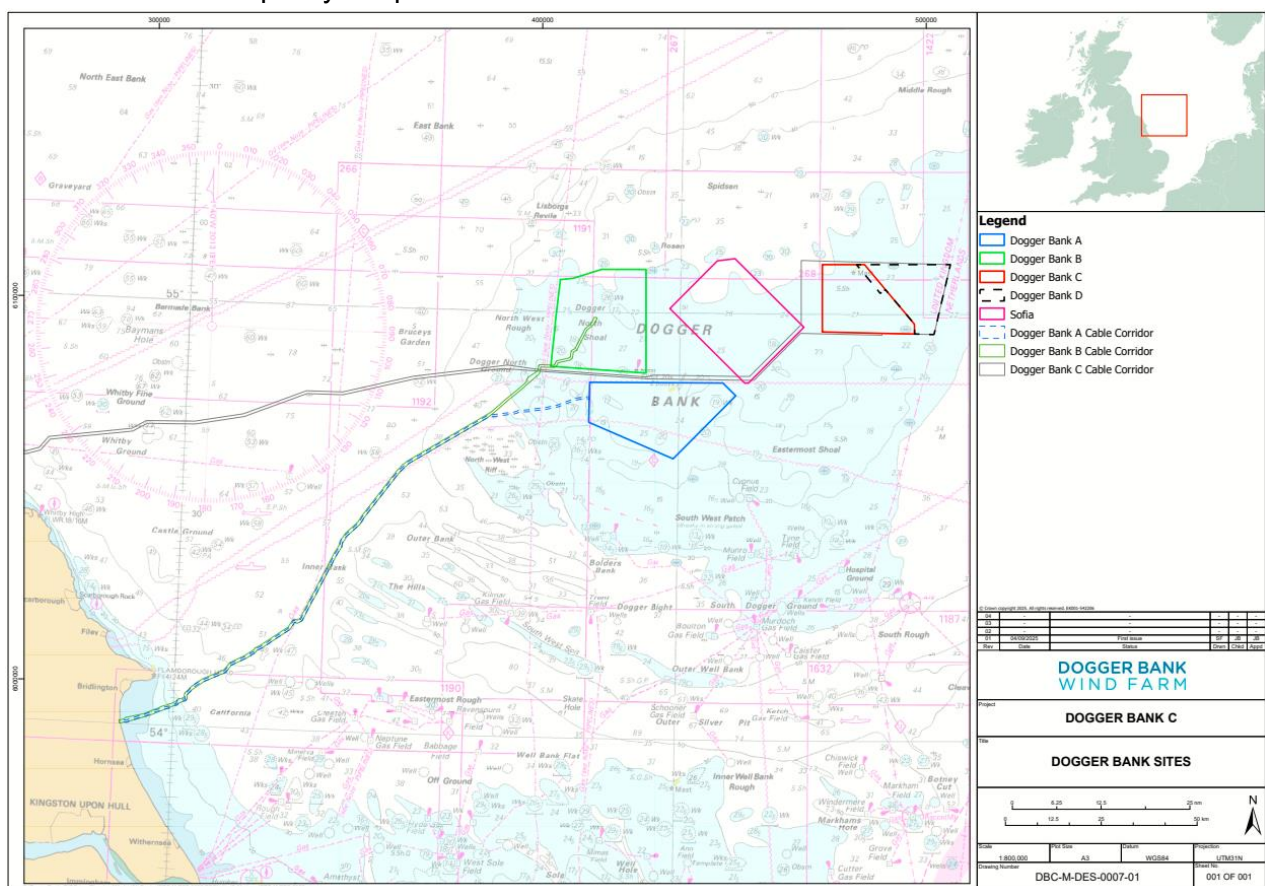


Figure 1 Dogger Bank C Offshore Wind Farm Location

Weekly Notice of Operations (WNoO)

Dogger Bank C Offshore Windfarm

Construction Operations

DOGGER BANK
WIND FARM

Issue Date: 20th June 2026

LF700013-CST-DOG-NOT-0099 Weekly Notice of Operations – Rev 095

1. Contact Details for Marine Coordination

The following contact can provide more information if required. Please note that specific queries can also be addressed to the relevant vessel or shore-based representatives.

Duty Marine Coordinator Telephone Number	+44 (0) 7586 332078
Emergency Contact (24/7)	+44 (0) 7586 332078
Email for Marine Coordinator	gm_dbmcc@equinor.com
Address	Dogger Bank MCC, Dogger Bank Operations & Maintenance Base, Enterprise Way, East Side, Port of Tyne, South Shields NE33 5SW

2. Ongoing Operations

2.1 Inter-Array Cable Installation Operations

The Cable Lay Vessel (CLV) **Viking Neptun** will continue cable installation operations.

The Service Operations Vessels (SOV) **Wind Evolution** and **Norside Cygnus** will continue inter-array cable installation support operations.

The Multi-Purpose Offshore Vessel **Grand Canyon II** will arrive to continue inter-array cable post lay burial operations.

The Fall-Pipe Rock Installation Vessel **Flintstone** will arrive to install scour protection at various locations.

During operations, all vessels will be restricted in their ability to manoeuvre as defined under COLREGs (International Regulations for Preventing Collisions at Sea 1972) and will display the appropriate day shapes and lights. The vessels will also transmit an Automatic Identification System (AIS) message.

It is requested that all vessels maintain a minimum of 500m separation distance from the working vessels and pass at reduced speed. Fishing gear or other equipment with seabed intervention should not be deployed when approaching the working area

3. Installation progress

3.1 All Monopile / Transition Pieces (MP/TP) in the DBC construction site have now been installed

3.2 The table and diagram below present the locations of the DBC Inter Array Cable (IAC) locations and gives an update on the progress of installation of various stages of construction.

Weekly Notice of Operations (WNoO)

Dogger Bank C Offshore Windfarm

Construction Operations

Issue Date: 20th June 2026

LF700013-CST-DOG-NOT-0099 Weekly Notice of Operations – Rev 095

String	Cable ID	From	To	Cable Laid	Cable Buried
A	DCA1	DC OSP	DCE04 AA	Y	Y
	DCA2	DCE04 AA	DCF04 AB	Y	Y
	DCA3	DCF04 AB	DCF03 AC	Y	Y
	DCA4	DCF03 AC	DCP05 AD	Y	Y
	DCA5	DCP05 AD	DBP06 AE	Y	Y
	DCA6	DBP06 AE	DBP07 AF	Y	Y
String	Cable ID	From	To	Cable Laid	Cable Buried
B	DCB1	DC OSP	DCE03 BA	Y	
	DCB2	DCE03 BA	DCF02 BB	Y	Y
	DCB3	DCF02 BB	DCF01 BC	Y	Y
	DCB4	DCF01 BC	DCP09 BD	Y	Y
	DCB5	DCP09 BD	DCP08 BE	Y	Y
String	Cable ID	From	To	Cable Laid	Cable Buried
C	DCC1	DB OSP	DCE02 CA	Y	
	DCC2	DCE02 CA	DCE01 CB	Y	Y
	DCC3	DCE01 CB	DCP12 CC	Y	Y
	DCC4	DCP12 CC	DCP11 CD	Y	Y
	DCC5	DCP11 CD	DCP10 CE	Y	Y
String	Cable ID	From	To	Cable Laid	Cable Buried
D	DCD1	DC OSP	DCD04 DA	Y	
	DCD2	DCD04 DA	DCD03 DB	Y	Y
	DCD3	DCD03 DB	DCD02 DC	Y	Y
	DCD4	DCD02 DC	DCD01 DD	Y	Y
	DCD5	DCD01 DD	DCP14 DE	Y	Y
	DCD6	DCP14 DE	DCP13 DF	Y	Y
String	Cable ID	From	To	Cable Laid	Cable Buried
E	DCE1	DC OSP	DCC01 EA	Y	Y
	DCE2	DCC01 EA	DCP18 EB	Y	Y
	DCE3	DCP18 EB	DCP17 EC	Y	Y
	DCE4	DCP17 EC	DCP16 ED	Y	Y
	DCE5	DCP16 ED	DCP15 EE	Y	Y

String	Cable ID	From	To	Cable Laid	Cable Buried
F	DCF1	DC OSP	DCC02 FA	Y	
	DCF2	DCC02 FA	DCB01 FB		
	DCF3	DCB01 FB	DCP21 FC		
	DCF4	DCP21 FC	DCP20 FD		
	DCF5	DCP20 FD	DCP19 FE		
String	Cable ID	From	To	Cable Laid	Cable Buried

Weekly Notice of Operations (WNoO)

Dogger Bank C Offshore Windfarm

Construction Operations

Issue Date: 20th June 2026

LF700013-CST-DOG-NOT-0099 Weekly Notice of Operations – Rev 095

G	DCG1	DC OSP	DCC03 GA	Y	
	DCG2	DCC03 GA	DCB02 GB		
	DCG3	DCB02 GB	DCP22 GC		
	DG4	DCP22 GC	DCP23 GD		
	DCG5	DCP23 GD	DCP24 GE		
String	Cable ID	From	To	Cable Laid	Cable Buried
H	DCH1	DC OSP	DCC04 HA	Y	
	DCH2	DCC04 HA	DCB03 HB		
	DCH3	DCB03 HB	DCA01 HC		
	DCH4	DCA01 HC	DCP27 HD		
	DCH5	DCP27 HD	DCP26 HE		
	DCH6	DCP26 HE	DCP25 HF		
String	Cable ID	From	To	Cable Laid	Cable Buried
J	DCJ1	DC OSP	DCC05 JA	Y	
	DCJ2	DCC05 JA	DCB04 JB	Y	
	DCJ3	DCB04 JB	DCP28 JC	Y	
	DCJ4	DCP28 JC	DCP29 JD		
	DCJ5	DCP29 JD	DCP30 JE		
	DCJ6	DCP30 JE	DCP31 JF		
String	Cable ID	From	To	Cable Laid	Cable Buried
K	DCK1	DC OSP	DC06 KA	Y	
	DCK2	DCC06 KA	DCC07 KB		
	DCK3	DCC07 KB	DCP32 KC	Y	
	DCK4	DCP32 KC	DCP33 KD	Y	
	DCK5	DBP33 KD	DBP34 KE	Y	
	DCK6	DBP34 KE	DBP35 KF	Y	
String	Cable ID	From	To	Cable Laid	Cable Buried
L	DCL1	DC OSP	DCD07 LA		
	DCL2	DCD07 LA	DCD08 LB	Y	
	DCL3	DCD08 LB	DCD09 LC	Y	
	DCL4	DCD09 LC	DCD10 LD	Y	
	DCL5	DCD10 LD	DCD11 LE	Y	
String	Cable ID	From	To	Cable Laid	Cable Buried
M	DCM1	DC OSP	DCD06 MA		
	DCM2	DCD06 MA	DCE12 MB	Y	
	DCM3	DCE12 MB	DCP39 MC	Y	
	DCM4	DCP39 MC	DCP38 MD	Y	
	DCM5	DCP38 MD	DCP37 ME	Y	
	DCM6	DCP37 ME	DCP36 MF	Y	
String	Cable ID	From	To	Cable Laid	Cable Buried
N	DCN1	DC OSP	DCE09 NA		

Weekly Notice of Operations (WNoO)

Dogger Bank C Offshore Windfarm

Construction Operations

Issue Date: 20th June 2026

LF700013-CST-DOG-NOT-0099 Weekly Notice of Operations – Rev 095

	DCN2	DCE09 NA	DCE10 NB	Y	
	DCN3	DCE10 NB	DCE11 NC	Y	
	DCN4	DCE11 NC	DCF12 ND	Y	
	DCN5	DCF12 ND	DCP41 NE	Y	
	DCN6	DCP41 NE	DCP40 NF	Y	
String	Cable ID	From	To	Cable Laid	Cable Buried
P	DCP1	DC OSP	DCE07 PA		
	DCP2	DCE07 PA	DCF08 PB		
	DCP3	DCF08 PB	DCF09 PC	Y	
	DCP4	DCF09 PC	DCF10 PD	Y	
	DCP5	DCF10 PD	DCF11 PE	Y	
String	Cable ID	From	To	Cable Laid	Cable Buried
Q	DCQ1	DC OSP	DCE06 QA		
	DCQ2	DCE06 QA	DCF07 QB	Y	
	DCQ3	DCF07 QB	DCP47 QC		
	DCQ4	DCP47 QC	DCP01 QD		
	DCQ5	DCP01 QD	DCP02 QE		
String	Cable ID	From	To	Cable Laid	Cable Buried
R	DCR1	DC OSP	DCE05 RA		
	DCR2	DCE05 RA	DCF05 RB		
	DCR3	DCF06 RB	DCF06 RC		
	DCR4	DCF05 RC	DCP03 RD		
	DCR5	DCP03 RD	DCP04 RE		

Weekly Notice of Operations (WNoO)


Dogger Bank C Offshore Windfarm

Construction Operations



Issue Date: 20th June 2026

LF700013-CST-DOG-NOT-0099 Weekly Notice of Operations – Rev 095

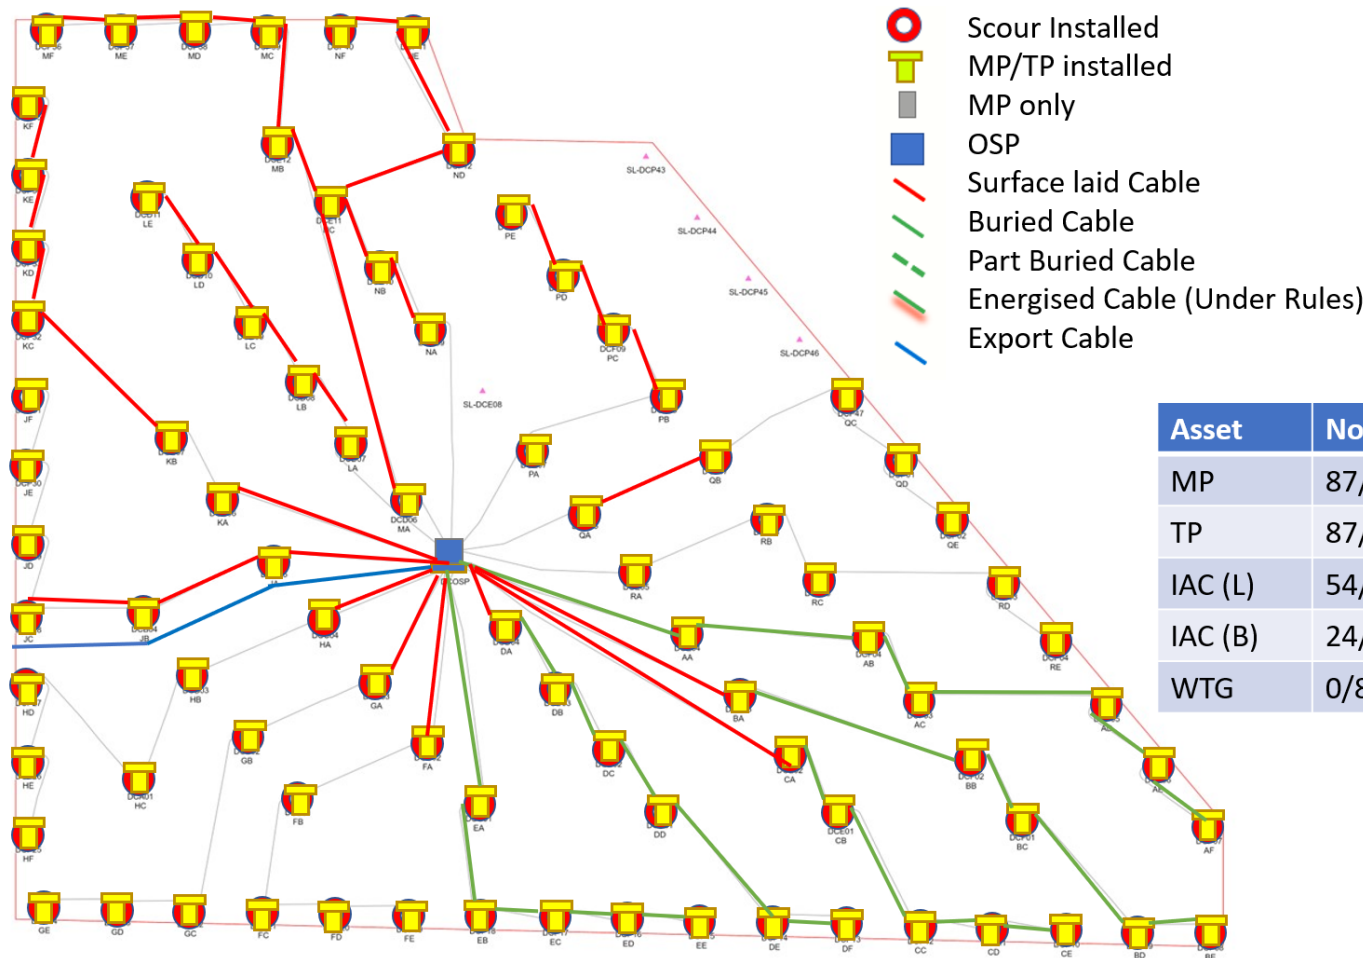

Asset	No
MP	87/87
TP	87/87
IAC (L)	54/87
IAC (B)	24/87
WTG	0/87

Weekly Notice of Operations (WNoO)

Dogger Bank C Offshore Windfarm

Construction Operations

DOGGER BANK
WIND FARM

Issue Date: 20th June 2026

LF700013-CST-DOG-NOT-0099 Weekly Notice of Operations – Rev 095

4. General Safety Advice

All vessels engaged in construction activities will exhibit the appropriate lights and shapes, defined by the International Regulations for Preventing Collisions at Sea 1972, relative to their operations. Vessels will also transmit an Automatic Identification System (AIS) message.

5. Safety Zones within the Dogger Bank Offshore Windfarm Construction Area

The Secretary of State for Business, Energy and Industrial Strategy (BEIS) has approved the use of safety zones under the Energy Act 2004 for the installation of wind turbines and offshore transformer module foundations/substructures within the Dogger Bank Offshore Windfarm.

The Secretary of State has declared safety zones under the following terms:

During Construction

- 500 metres radius around each wind turbine, offshore transformer module and/or their substructures and foundations comprising the Dogger Bank Offshore Wind Farm whilst work is being performed as indicated by the presence of construction vessels.

(It is noted that the 500 metre safety zones will roll with the installation activity with no more than two construction vessels working at any one time. Vessels are advised that anchors associated with the construction vessels may extend outside of the 500 metre safety zone.)

- 50 metres radius around each wind turbine, offshore transformer module and/or their substructure and foundations installed but waiting to be commissioned as part of the Dogger Bank Offshore Wind Farm.

Positions of foundations installed will be published in the current Weekly Notice of Operations. Only vessels associated with the Dogger Bank Offshore Wind Farm construction may enter statutory safety zones.

The guard vessel and Marine Coordination centre will be responsible for monitoring and policing the safety zones; and can be contacted directly for advice. The guard vessel will be on site 24/7 whilst safety zones are in place.

Further information on the application of safety zones can be obtained from the Marine Coordinator. Users are advised to keep clear of construction activities, including safety zones, within the Dogger Bank Offshore Windfarm construction area in line with Marine Guidance Note (MGN) 372.

ALL VESSELS ARE REQUESTED to give all construction and support vessels a wide berth.

Weekly Notice of Operations (WNoO)

Dogger Bank C Offshore Windfarm Construction Operations

DOGGER BANK
WIND FARM

Issue Date: 20th June 2026

LF700013-CST-DOG-NOT-0099 Weekly Notice of Operations – Rev 095

MARINERS ARE REMINDED to navigate with caution and keep continued watch on VHF Ch. 70 / 16 when navigating the area

6. Fisheries Liaison

Fisheries liaison associated with the activity will be co-ordinated by Brown and May Marine Ltd. For any commercial fishery queries please contact:

Alex Winrow-Giffin, Brown & May Marine Ltd

Alex@brownmay.com

Tel: 01379 870181 Mob: 07760 160039

Zoë Lawrence - Brown & May Marine Ltd

zoe@brownmay.com

Mob: 07923 138175

The Export Cable installation campaign is anticipated to be completed ~ April 2025.

7. Distribution List

A central list of recipients is maintained by the Marine Coordinator. If you are not the appropriate recipient of these notices or do not wish to receive the notices in the future, please contact us at the address included in Section 1 of this notice.

8. Website

The official website of Dogger Bank Offshore Windfarm Limited can be found at:

[Weekly documents Archive - Dogger Bank Wind Farm](#)

This contains all Notices to Mariners (NtM) published by DBOWF and all Weekly Notices of Operations, together with a large amount of general information about the Project.

Details of NtM published by DBOWF can also be found on the Kingfisher Bulletin interactive chart at:

[View all Notices \(kingfisherbuletin.org\)](http://kingfisherbuletin.org)

Weekly Notice of Operations (WNoO)

Dogger Bank C Offshore Windfarm

Construction Operations

DOGGER BANK
WIND FARM

Issue Date: 20th June 2026

LF700013-CST-DOG-NOT-0099 Weekly Notice of Operations – Rev 095

Vessels & Operators									
Vessel Data Matrix DBC OWF									
No	Vessel Picture	Vessel Name / Flag	Type / Function	Operator	Contact / contact details	Call sign / MMSI / IMO	LOA (m) Beam (m) Draft (m)	Date on Site	Marine Licence applicable
2		Wind Evolution GB	Service Operations Vessel	Transnautic Ship Management	Toomas Huudma DPA Transnautic Ship Management +372 5015 899	MOYX5 / 232054319 / 9730505	80m x 18.4m x 3.8m	20.06.2026	OFTO/Non-OFTO
3		Norside Cygnus BH	Service Operations Vessel	Norside Wind AS	Brutus Ophalvens (DEME HSE Manager) Mobile: +32 489 39 89 90 Email: Ophalvens.Brutus@dem-group.com	C6BW7 / 311000386 / 9714214	85.6m x 22.5 m x 5.5m	12.06.2026	OFTO/Non-OFTO
4		Grand Canyon II NO	Multi Purpose Offshore Vessel	Helix	Brutus Ophalvens (DEME HSE Manager) Mobile: +32 489 39 89 90 Email: Ophalvens.Brutus@dem-group.com	LACY8 / 257038580 / 9653874	125M X 25M X 8.4M	22.07.2026	OFTO/Non-OFTO
5		Flintstone	Fall pipe rock installation	DEME	Brutus Ophalvens (DEME HSE Manager) Mobile: +32 489 39 89 90 Email: Ophalvens.Brutus@dem-group.com	PBZD / 245861000 / 9528433	154.6m x 32.2m x 7.74m	23.07.2026	Non-OFTO & OFTO
